
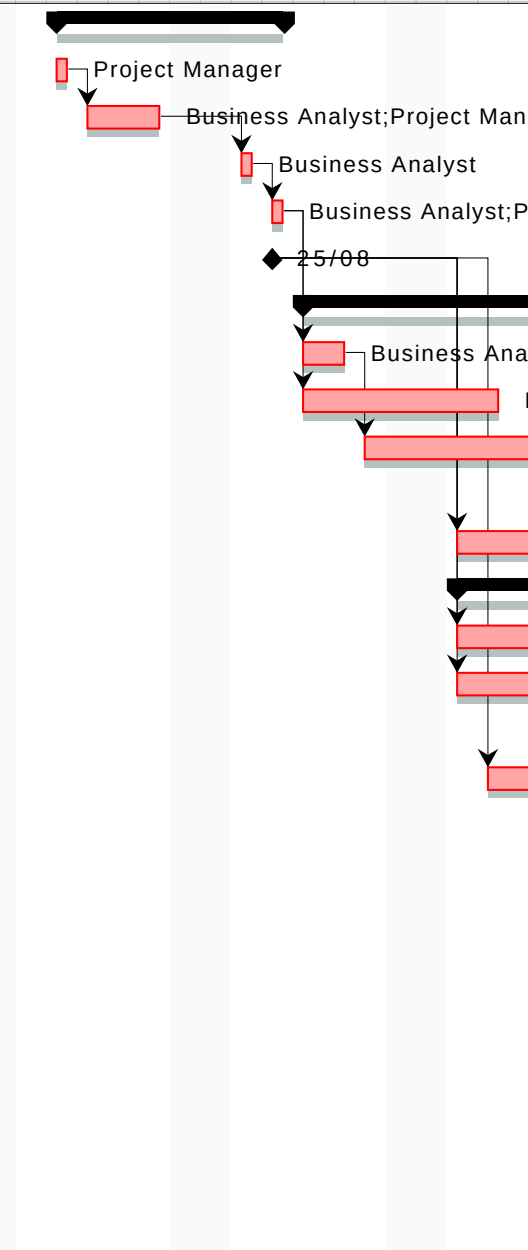


		WBS	Name	Start	Finish	Baseline Start	Baseline Finish
1		1.0	Project Initiation and Selection	18/08/26 8:00 AM	25/08/26 5:00 PM	18/08/26 8:00 AM	25/08/26 5:00 PM
2		1.1	Group Formation and Role Allocation	18/08/26 8:00 AM	18/08/26 5:00 PM	18/08/26 8:00 AM	18/08/26 5:00 PM
3		1.2	Review of Proposed Projects	19/08/26 8:00 AM	21/08/26 5:00 PM	19/08/26 8:00 AM	21/08/26 5:00 PM
4		1.3	Weighted Scoring Evaluation	24/08/26 8:00 AM	24/08/26 5:00 PM	24/08/26 8:00 AM	24/08/26 5:00 PM
5		1.4	Project Selection and Justification	25/08/26 8:00 AM	25/08/26 5:00 PM	25/08/26 8:00 AM	25/08/26 5:00 PM
6		1.5	Week 5 Progress Presentation	25/08/26 8:00 AM	25/08/26 8:00 AM	25/08/26 8:00 AM	25/08/26 8:00 AM
7		2.0	Business Analysis and Project Pla...	26/08/26 8:00 AM	4/09/26 5:00 PM	26/08/26 8:00 AM	4/09/26 5:00 PM
8		2.1	Current Situation Analysis	26/08/26 8:00 AM	27/08/26 5:00 PM	26/08/26 8:00 AM	27/08/26 5:00 PM
9		2.2	Business Case Development	26/08/26 8:00 AM	1/09/26 5:00 PM	26/08/26 8:00 AM	1/09/26 5:00 PM
10		2.3	Cost-Benefit and Financial Analysis	28/08/26 8:00 AM	2/09/26 5:00 PM	28/08/26 8:00 AM	2/09/26 5:00 PM
11		2.4	Feasibility Analysis	3/09/26 8:00 AM	3/09/26 5:00 PM	3/09/26 8:00 AM	3/09/26 5:00 PM
12		2.5	Project Charter Development	31/08/26 8:00 AM	4/09/26 5:00 PM	31/08/26 8:00 AM	4/09/26 5:00 PM
13		3.0	Requirements and Scope Manage...	31/08/26 8:00 AM	11/09/26 5:00 PM	31/08/26 8:00 AM	11/09/26 5:00 PM
14		3.1	Functional Requirements	31/08/26 8:00 AM	2/09/26 5:00 PM	31/08/26 8:00 AM	2/09/26 5:00 PM
15		3.2	Non-Functional Requirements	31/08/26 8:00 AM	2/09/26 5:00 PM	31/08/26 8:00 AM	2/09/26 5:00 PM
16		3.3	Project Scope Statement	3/09/26 8:00 AM	7/09/26 5:00 PM	3/09/26 8:00 AM	7/09/26 5:00 PM
17		3.4	Stakeholder Analysis	1/09/26 8:00 AM	3/09/26 5:00 PM	1/09/26 8:00 AM	3/09/26 5:00 PM
18		3.5	Communication Plan	4/09/26 8:00 AM	8/09/26 5:00 PM	4/09/26 8:00 AM	8/09/26 5:00 PM
19		3.6	Project Exclusions and Coonstraints	7/09/26 8:00 AM	8/09/26 5:00 PM	7/09/26 8:00 AM	8/09/26 5:00 PM
20		3.7	Acceptance Criteria	9/09/26 8:00 AM	11/09/26 5:00 PM	9/09/26 8:00 AM	11/09/26 5:00 PM
21		4.0	Project Schedule, Risk and Cost Pl...	14/09/26 8:00 AM	25/09/26 5:00 PM	14/09/26 8:00 AM	25/09/26 5:00 PM
22		4.1	Work Breakdown Structure	14/09/26 8:00 AM	15/09/26 5:00 PM	14/09/26 8:00 AM	15/09/26 5:00 PM
23		4.2	WBS Dictionary	16/09/26 8:00 AM	16/09/26 5:00 PM	16/09/26 8:00 AM	16/09/26 5:00 PM
24		4.3	ProjectLibre Schedule	16/09/26 8:00 AM	18/09/26 5:00 PM	16/09/26 8:00 AM	18/09/26 5:00 PM
25		4.4	Risk Identification and Analysis	14/09/26 8:00 AM	18/09/26 5:00 PM	14/09/26 8:00 AM	18/09/26 5:00 PM
26		4.5	Risk Response Planning	21/09/26 8:00 AM	22/09/26 5:00 PM	21/09/26 8:00 AM	22/09/26 5:00 PM
27		4.6	Effort Estimation	21/09/26 8:00 AM	23/09/26 5:00 PM	21/09/26 8:00 AM	23/09/26 5:00 PM
28		4.7	Cost Estimation	23/09/26 8:00 AM	25/09/26 5:00 PM	23/09/26 8:00 AM	25/09/26 5:00 PM

Duration	Predecessors	Resource Names	Cost	16 Aug 26							23 Aug 26							30 Aug 26													
				S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S						
6 days			\$8000.00																												
1 day		Project Manager	\$880.00																												
3 days	2	Business Analyst;Project Manager	\$4800.00																												
1 day	3	Business Analyst	\$720.00																												
1 day	4	Business Analyst;Project Manager	\$1600.00																												
0 days		Business Analyst;Project Manager	\$0.00																												
8 days			\$17400.00																												
2 days	5	Business Analyst	\$1440.00																												
5 days	5	Business Analyst	\$3600.00																												
4 days	8	Business Analyst	\$2880.00																												
1 day	10	Business Analyst;Systems Analyst	\$1480.00																												
5 days	6	Business Analyst;Project Manager	\$8000.00																												
10 days			\$30680.00																												
3 days	6	Business Analyst	\$2160.00																												
3 days	6	Business Analyst;Systems Analyst	\$4440.00																												
3 days	14;15	Business Analyst;Project Manager	\$4800.00																												
3 days	6	Business Analyst;Project Manager	\$4800.00																												
3 days	17	Business Analyst;Project Manager	\$4800.00																												
2 days	16	Business Analyst;Project Manager	\$3200.00																												
3 days	16;19	Business Analyst;Systems Analyst;Test Analyst	\$6480.00																												
10 days			\$32960.00																												
2 days	20	Business Analyst;Project Manager	\$3200.00																												
1 day	22	Business Analyst;Systems Analyst	\$1480.00																												
3 days	22	Project Manager;Systems Analyst	\$4920.00																												
5 days	20	Project Manager;Systems Analyst	\$8200.00																												
2 days	25	Project Manager;Systems Analyst	\$3280.00																												
3 days	23;24	Business Analyst;Project Manager;Systems Analyst	\$7080.00																												
3 days	27	Business Analyst;Project Manager	\$4800.00																												

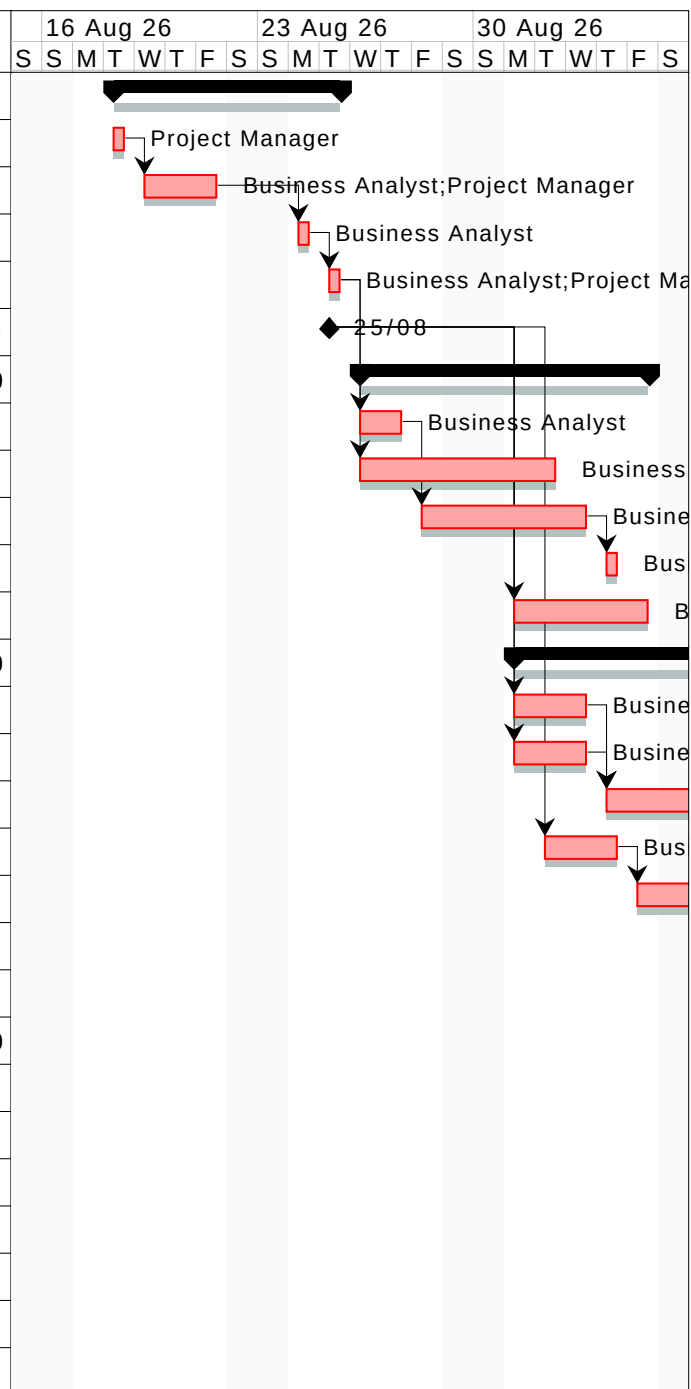

[illegible]

		WBS	Name	Start	Finish	Baseline Start	Baseline Finish
29		5.0	User Interface and Prototype Desi...	21/09/26 8:00 AM	25/09/26 5:00 PM	21/09/26 8:00 AM	25/09/26 5:00 PM
30		5.1	Main Screen Design	21/09/26 8:00 AM	22/09/26 5:00 PM	21/09/26 8:00 AM	22/09/26 5:00 PM
31		5.2	Facility Search and Availability Scre...	22/09/26 8:00 AM	23/09/26 5:00 PM	22/09/26 8:00 AM	23/09/26 5:00 PM
32		5.3	Booking Request Screen	23/09/26 8:00 AM	24/09/26 5:00 PM	23/09/26 8:00 AM	24/09/26 5:00 PM
33		5.4	Conflict Detection and Validation D...	24/09/26 8:00 AM	24/09/26 5:00 PM	24/09/26 8:00 AM	24/09/26 5:00 PM
34		5.5	Approval/Rejection Screen	24/09/26 8:00 AM	25/09/26 5:00 PM	24/09/26 8:00 AM	25/09/26 5:00 PM
35		5.6	Maintenance and Reporting Interfa...	23/09/26 8:00 AM	25/09/26 5:00 PM	23/09/26 8:00 AM	25/09/26 5:00 PM
36		5.7	End-to-End Bookig Workflow Review	25/09/26 8:00 AM	25/09/26 5:00 PM	25/09/26 8:00 AM	25/09/26 5:00 PM
37		6.0	Functional Prototype Development	5/10/26 8:00 AM	9/10/26 5:00 PM	5/10/26 8:00 AM	9/10/26 5:00 PM
38		6.1	Development Environment Setup	5/10/26 8:00 AM	5/10/26 5:00 PM	5/10/26 8:00 AM	5/10/26 5:00 PM
39		6.2	Facility Search Function	5/10/26 8:00 AM	6/10/26 5:00 PM	5/10/26 8:00 AM	6/10/26 5:00 PM
40		6.3	Availability Checking Function	6/10/26 8:00 AM	7/10/26 5:00 PM	6/10/26 8:00 AM	7/10/26 5:00 PM
41		6.4	Booking Request Function	7/10/26 8:00 AM	7/10/26 5:00 PM	7/10/26 8:00 AM	7/10/26 5:00 PM
42		6.5	Conflict Detection Function	8/10/26 8:00 AM	8/10/26 5:00 PM	8/10/26 8:00 AM	8/10/26 5:00 PM
43		6.6	Staff Approval/Rejection Function	8/10/26 8:00 AM	9/10/26 5:00 PM	8/10/26 8:00 AM	9/10/26 5:00 PM
44		6.7	Booking Result and User Feedback	9/10/26 8:00 AM	9/10/26 5:00 PM	9/10/26 8:00 AM	9/10/26 5:00 PM
45		6.8	Sample Data and Input Validation	6/10/26 8:00 AM	8/10/26 5:00 PM	6/10/26 8:00 AM	8/10/26 5:00 PM
46		6.9	Prototype Integration	9/10/26 8:00 AM	9/10/26 5:00 PM	9/10/26 8:00 AM	9/10/26 5:00 PM
47		7.0	Testing, Change Management and...	12/10/26 8:00 AM	16/10/26 5:00 PM	12/10/26 8:00 AM	16/10/26 5:00 PM
48		7.1	Change request Analysis	12/10/26 8:00 AM	12/10/26 5:00 PM	12/10/26 8:00 AM	12/10/26 5:00 PM
49		7.2	Approved Change Implementation	13/10/26 8:00 AM	13/10/26 5:00 PM	13/10/26 8:00 AM	13/10/26 5:00 PM
50		7.3	Test Plan Preparation	12/10/26 8:00 AM	12/10/26 5:00 PM	12/10/26 8:00 AM	12/10/26 5:00 PM
51		7.4	Functional Testing	14/10/26 8:00 AM	14/10/26 5:00 PM	14/10/26 8:00 AM	14/10/26 5:00 PM
52		7.5	Integration Testing	14/10/26 8:00 AM	15/10/26 5:00 PM	14/10/26 8:00 AM	15/10/26 5:00 PM
53		7.6	Bug Fixing and retesting	15/10/26 8:00 AM	15/10/26 5:00 PM	15/10/26 8:00 AM	15/10/26 5:00 PM
54		7.7	ProjectLibre Progress Update	15/10/26 8:00 AM	15/10/26 5:00 PM	15/10/26 8:00 AM	15/10/26 5:00 PM
55		7.8	Final Report Compilation	15/10/26 8:00 AM	16/10/26 5:00 PM	15/10/26 8:00 AM	16/10/26 5:00 PM
56		8.0	Project Closure and Submission	15/10/26 8:00 AM	20/10/26 8:00 AM	15/10/26 8:00 AM	20/10/26 8:00 AM

Duration	Predecessors	Resource Names	Cost	16 Aug 26							23 Aug 26							30 Aug 26						
				S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
5 days			\$16600.00																					
2 days	20	UX Designer	\$1360.00																					
2 days	30	Business Analyst;UX Designer	\$2800.00																					
2 days	31	Business Analyst;UX Designer	\$2800.00																					
1 day	32	Systems Analyst;UX Designer	\$1440.00																					
2 days	32	UX Designer	\$1360.00																					
3 days	30	Data and Integration Specialist;UX Designer	\$4680.00																					
1 day	31;32;33;34	Business Analyst;Systems Analyst;UX Designer	\$2160.00																					
5 days			\$28840.00																					
1 day	36	Data and Integration Specialist;Software Developer	\$1680.00																					
2 days	38	Data and Integration Specialist;Software Developer	\$3360.00																					
2 days	39	Data and Integration Specialist;Software Developer;Systems ...	\$4880.00																					
1 day	40	Data and Integration Specialist;Software Developer	\$1680.00																					
1 day	41	Data and Integration Specialist;Software Developer;Systems ...	\$2440.00																					
2 days	42	Software Developer	\$1600.00																					
1 day	43	Data and Integration Specialist;Software Developer;Training...	\$3000.00																					
3 days	38	Data and Integration Specialist;Software Developer;Test Ana...	\$7080.00																					
1 day	44;45	Data and Integration Specialist;Software Developer;Systems ...	\$3120.00																					
5 days			\$18400.00																					
1 day	46	Business Analyst;Project Manager	\$1600.00																					
1 day	48	Software Developer;Systems Analyst	\$1560.00																					
1 day	46	Test Analyst	\$680.00																					
1 day	49;50	Software Developer;Test Analyst	\$1480.00																					
2 days	51	Data and Integration Specialist;Software Developer;Systems ...	\$6240.00																					
1 day	52	Software Developer;Test Analyst	\$1480.00																					
1 day	53	Project Manager	\$880.00																					
2 days	53	Business Analyst;Project Manager;Training/Support Specialist	\$4480.00																					
3 days			\$10640.00																					

[illegible]

		WBS	Name	Start	Finish	Baseline Start	Baseline Finish
57		8.1	Final Prototype Review	15/10/26 8:00 AM	15/10/26 5:00 PM	15/10/26 8:00 AM	15/10/26 5:00 PM
58		8.2	Final Project Documentation	15/10/26 8:00 AM	16/10/26 5:00 PM	15/10/26 8:00 AM	16/10/26 5:00 PM
59		8.3	GitHub and Contribution Evidence	16/10/26 8:00 AM	16/10/26 5:00 PM	16/10/26 8:00 AM	16/10/26 5:00 PM
60		8.4	Final Assessment Submission	16/10/26 8:00 AM	16/10/26 8:00 AM	16/10/26 8:00 AM	16/10/26 8:00 AM
61		8.5	Final Presentation and Demonstration	20/10/26 8:00 AM	20/10/26 8:00 AM	20/10/26 8:00 AM	20/10/26 8:00 AM

Duration	Predecessors	Resource Names	Cost	16 Aug 26							23 Aug 26							30 Aug 26						
				S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F
1 day		Data and Integration Specialist;Project Manager;Software De...	\$4640.00																					
2 days		Business Analyst;Project Manager;Training/Support Specialist	\$4480.00																					
1 day		Project Manager;Training/Support Specialist	\$1520.00																					
0 days		Project Manager;Test Analyst;Training/Support Specialist	\$0.00																					
0 days	60	Project Manager;Test Analyst;Training/Support Specialist	\$0.00																					

		15 Nov 26				
F	S	S	M	T	W	T
ems Analyst;Test A						
CSIT214 - pa...						
